BRUHAT BENGALURU MAHAN

	Clients Name	:
	Project Name	: Package2, includes 5 works of Rs.245.00 lakhs 1)Improvements to Roads and Drains at Mariyannapalya Balaji layout Near Railway Gate in Ward No:06 Byatarayanapura Sub Division. 3)Improvements to Dr and Asphalting to Roads at Bharathnagara saw mill Road in Ward No: 06 Byatarayanapura Sub Divisio
	Consultants	: Rudraprasad Consultants
	Project Manager /Team Leader	: Karthik Rechan
	Project Start Date	: 25-Jun-18
	Project End Date	: 25-Oct-18
	Project Length in Months	: 4 months

Sl. No	*Assignment*	*Unit*	*Boq Qnty*	*Qty of Work done*	*% Of Work done*	*Start Date*	*End Date*	*No. of Working Days*
1	Earthwork excavation by manual means in ordinary soil	Cum	2694.20	1613.89	60	27-06-18	23-10-18	118
2	Providing granite slabs of selected quality roughly dressed having a size of 7.5cms thick and fixed in cement mortar (1:6)	Sqm	3245.10	2312.88	71	10-07-18	23-10-18	105
3	Excavation for roadwork in soil with hydraulic excavator of 0.90 cum bucket capacity	Cum	3005.10	855.79	28	17-07-18	23-10-18	98
4	Providing,laying, spreading and compacting wet mix macadam	Cum	2854.20	855.79	30	23-07-18	23-10-18	92
5	Providing and applying primer coat with SS bitumen emulsion on prepared surface of granular Base such as WBM WMM including clearing of road surface	Sqm	12409.00	1952.57	16	30-07-18	23-10-18	85
6	Cleaning the existing black topped surface.	Sqm	27890.00	10918.29	39	03-08-18	23-10-18	81
7	Providing and applying tack coat using 80/100 grade bitumen (VG10) on prepared black topped surfaces	Sqm	32151.00	10918.29	34	07-08-18	23-10-18	77
8	Providing and laying bituminous concrete 40 mm	Cum	1286.00	436.73	34	07-08-18	23-10-18	77
9	Road Marking with Hot Applied Thermoplastic Compound with Reflectrising Glass Beads on Bituminous Surface	Sqm	1165.00	389.96	33	01-09-18	23-10-18	52
10	Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200mm	Sqm	260.00	0	0	0	0	0
11	Providing and removing centering, shuttering, strutting, propping etc., for columns, pillars, post and structs, square/rectangular/polygon in plan	Sqm	263.90	0	0	0	0	0
12	Providing and laying in position reinforced cement concrete of design mix M20	Cum	57.33	0	0	0	0	0
13	Providing T .M.T steel reinforcement for R.C.C work	tonne	2.87	0	0	0	0	0
14	Providing and laying in position plain cement concrete of mix 1:3:6	Cum	229.09	0	0	0	0	0
15	Construction of un-reinforced plain cement concrete pavement,thickness as per design, over a prepared sub base	Cum	139.38	0	0	0	0	0
16	Vaccum de-watering with vaccum pump and suction mat and compaction with skin floater	Sqm	1393.80	0	0	0	0	0

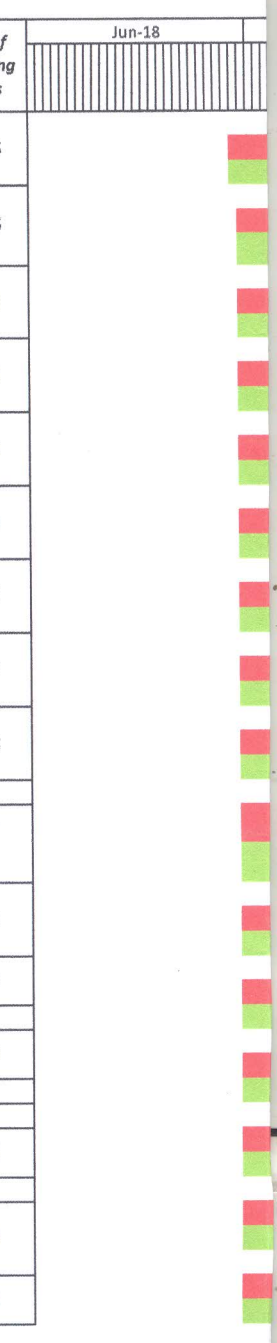

AGARA PALIKE

Executive Engineer Byatarayanapua Division

Church to Defence Layout and Dynasty Layout in Ward No:06 Byatarayanapura Sub Division. 2)Improvements to Drains and Asphalting to Roads at
s and Asphalting to Roads at Vidyasagara Layout and Surrounding area in Ward No: 06 Byatarayanapura Sub Division. 4)Improvements to Drains
5) Improvements to Drains and Asphalting to Roads at Shiradi Sai Nagar and Hegadenagar in Ward No:06 Byatarayanapura Sub Division.

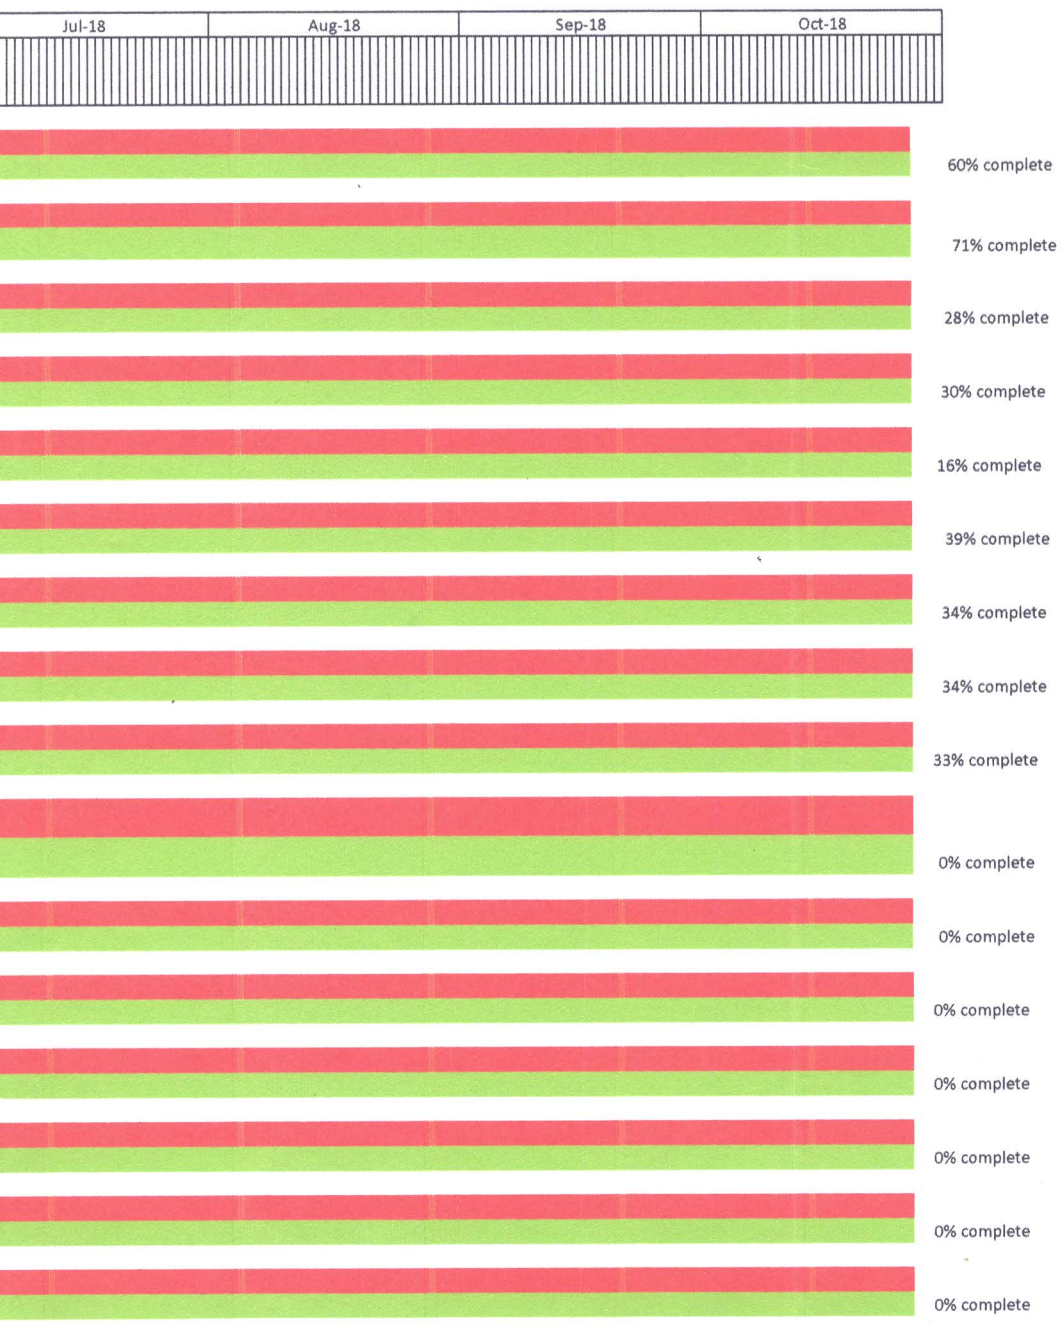

For RUDRAPRASAD CONSULTANTS

Partner./s.
